


ID	Task Name	Duration	Start	Finish	Predecessors	2007	2008	2009	2010									
						Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
1	COUNTY OF HAWAII - DWS - HOVE WELL PROJECT	0 days	Wed 7/19/06	Wed 7/19/06														
2	PHASE 1 AND 2	861 days	Wed 7/19/06	Wed 11/4/09	1													
3	Precontract Phase 1	123 days	Wed 7/19/06	Mon 1/8/07														
9	Determine 1st Location of Well	9 days	Fri 1/5/07	Wed 1/17/07	7													
10	Progress Topo- Well & Reservoir Site	12 wks	Fri 1/5/07	Thu 3/29/07	7													
11	Topo - Fill site and transmission line	6 wks	Fri 1/5/07	Thu 2/15/07	7													
12	Topo- New well site	27 days	Fri 2/16/07	Mon 3/26/07	11													
13	Preliminary Civil Work for EA	3 days	Fri 3/30/07	Tue 4/3/07	10													
14	Civil Conceptual Plan for EA	2 wks	Wed 4/4/07	Tue 4/17/07	7,13													
15	Well Design - Specs and drawings	101 days	Fri 1/5/07	Fri 5/25/07	7													
16	County/DWS Procurement for driller	78 days	Thu 7/5/07	Mon 10/22/07														
17	COH-DWS procurement process (follows FONSI determination by DWS below)	31 days	Thu 7/5/07	Thu 8/16/07	15													
18	Notice to Bidders Package Prep	8 days	Thu 7/5/07	Mon 7/16/07														
19	Contractors Pick up Bid Packages	0 days	Mon 7/16/07	Mon 7/16/07	18													
20	Pre-Bid meeting - 2 PM @ DWS	1 day	Wed 8/1/07	Wed 8/1/07	19													
21	Open bids	1 day	Thu 8/16/07	Thu 8/16/07	20													
22	DWS approval of bid and selection of contractor	0 days	Thu 8/16/07	Thu 8/16/07	21													
23	Contracting Process for Exploratory Well Contractor	30 edays	Thu 8/16/07	Sat 9/15/07	22													
24	Drilling Contract Signed	0 days	Sat 9/15/07	Sat 9/15/07	23													
25	Public Meeting (Second Meeting) - Tentative	1 day	Mon 10/22/07	Mon 10/22/07	24FS+25 days													
26	070323 HOVE ENV ASSESS	156 days	Mon 1/8/07	Mon 8/13/07														
27	Permitting Exp Well	67 days	Mon 5/28/07	Tue 8/28/07														
28	Prepare & Submit Well Permit Application	3 days	Mon 5/28/07	Wed 5/30/07	16													
29	Water Commission Processing	90 edays	Wed 5/30/07	Tue 8/28/07	28													
30	Water Commission Letter of Assurance	0 days	Tue 8/28/07	Tue 8/28/07	29													
31	Permit signed by Drilling Contractor	2 days	Mon 9/18/07	Tue 9/18/07	24,30													
32	Drill Exploratory Well	12 mons	Wed 9/19/07	Tue 8/19/08	31													
33	070613 HOVE Design Build	298 days	Mon 3/5/07	Wed 4/23/08														
1	Prepare Proposal	44 days	Mon 3/5/07	Thu 5/3/07														
2	DWS/COH Process Supp. Agmnt & Sign	26 days	Fri 5/4/07	Fri 6/8/07	1													
3	DAGS contract approval	19 days	Mon 6/11/07	Thu 7/5/07	2													
4	TASK 1: ESTABLISH PROJECT ORGANIZATION	13 days	Fri 7/6/07	Tue 7/24/07														
5	Identify PM & Team	5 days	Fri 7/6/07	Thu 7/12/07	3													
6	Review background	5 days	Fri 7/6/07	Thu 7/12/07	3													
7	Participate in data collection & orientation	8 days	Fri 7/6/07	Tue 7/17/07	3													
8	Establish Work Plan & Develop TOC for RFQ, RFP	5 days	Wed 7/18/07	Tue 7/24/07	7													
9	TASK 2: DEVELOP RFQ DOCUMENTATION	28 days	Wed 7/25/07	Wed 8/29/07	4													
10	Determine evaluation criteria & RFQ schedule	9 days	Wed 7/25/07	Mon 8/6/07														
11	Compose RFQ	9 days	Tue 8/7/07	Fri 8/17/07	10													
12	Submittal requirements	9 days	Tue 8/7/07	Fri 8/17/07														
13	Summary information regarding project	5 days	Tue 8/7/07	Mon 8/13/07														
14	Evaluation criteria	5 days	Tue 8/7/07	Mon 8/13/07														
15	Interim communications protocols	1 day	Tue 8/7/07	Tue 8/7/07														
16	Schedule for submittal, evaluation & short list notification	5 days	Tue 8/7/07	Mon 8/13/07														
17	Recommend Composition of RFQ Eval. Panel.	5 days	Mon 8/20/07	Fri 8/24/07	11													
18	Finalize RFQ list of panelists	3 days	Mon 8/27/07	Wed 8/29/07	17													
19	Compose legal advertisement for publication by DWS	5 days	Tue 8/14/07	Mon 8/20/07	16													

Project: 070821 MASTER HOVE  
Date: Fri 9/7/07

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

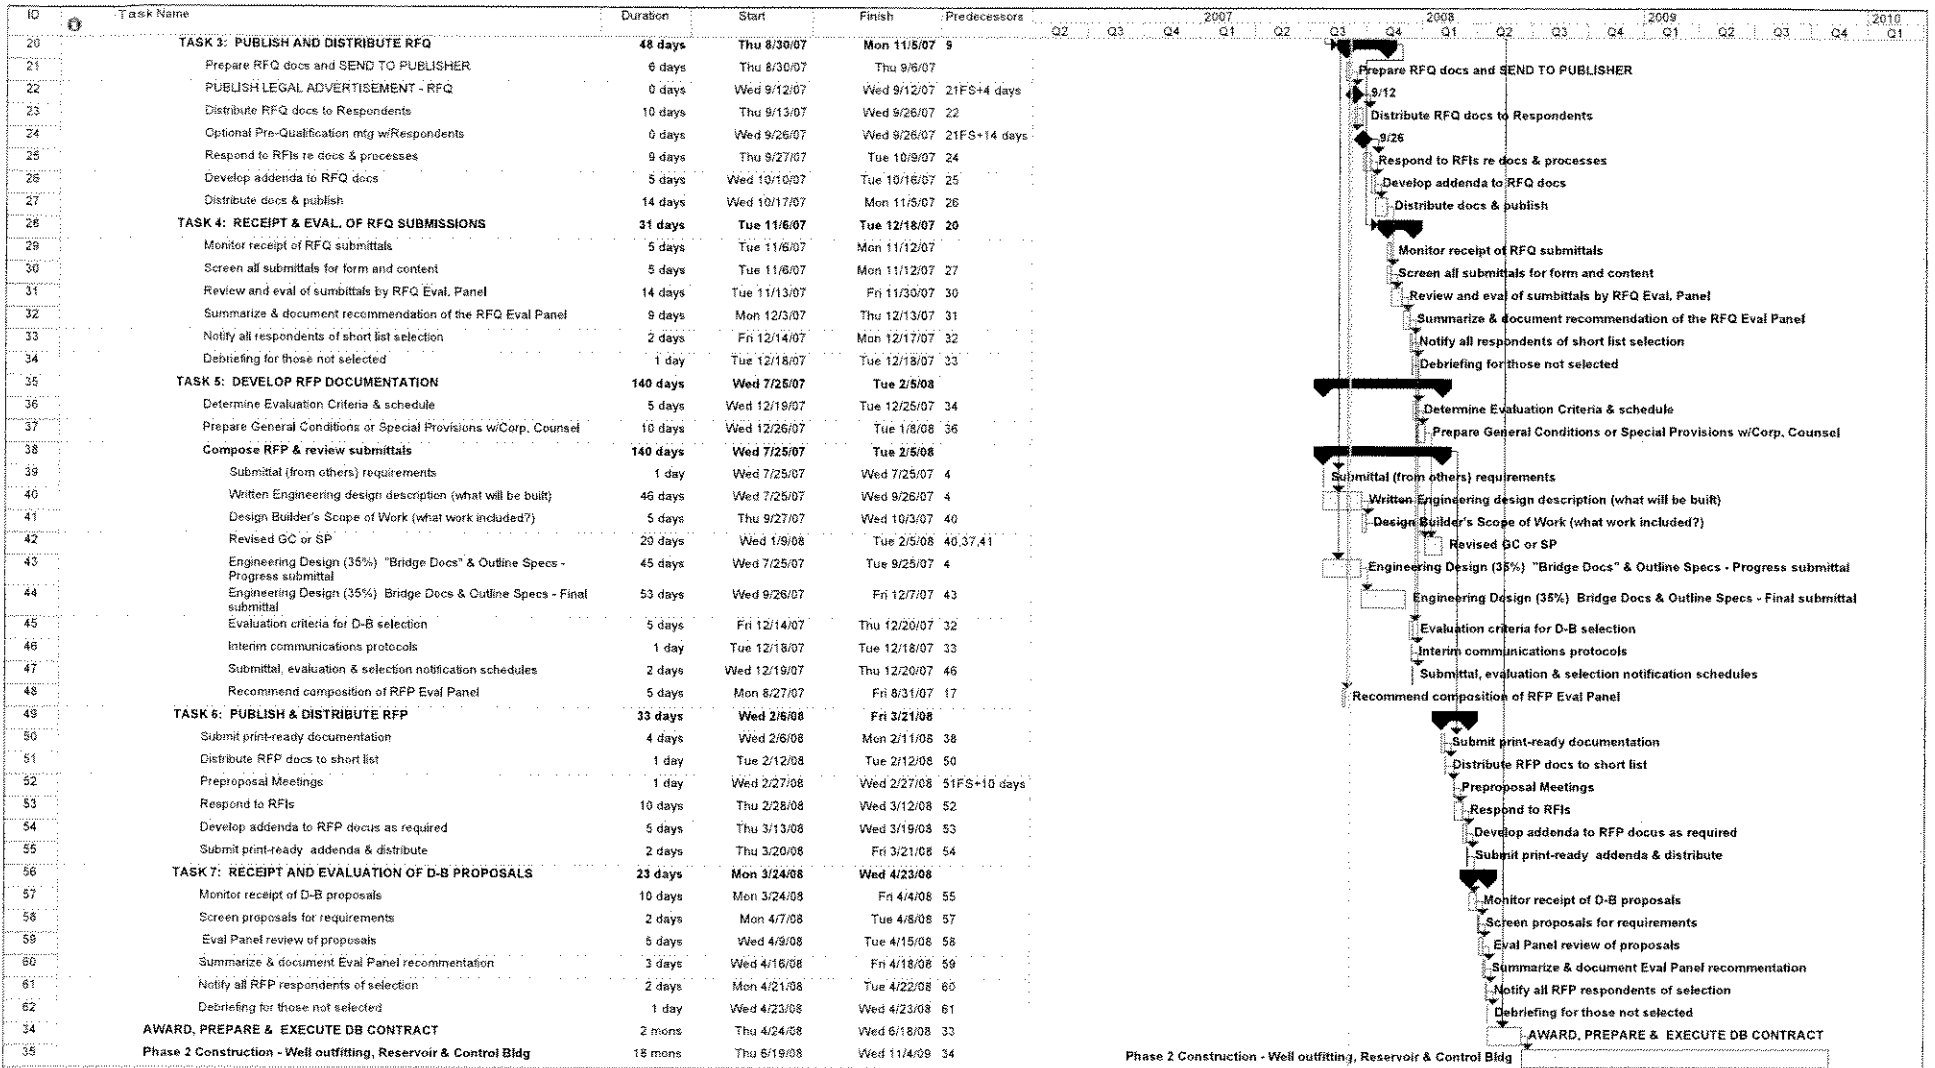

Project: 070821 MASTER HOVE  
Date: Fri 9/7/07

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone
